

TEST REPORT



Clients	Bruhat Bangalore Mahanagara Palike
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore
Contractor	M/s Sri. E Ramesh Anand

SIEVE ANALYSIS

Total Weight:	3000	gms			
Type of Material	Fine aggregate (M sand)		Proposed Use	Concrete	
Sample Location	At Plant		Date of Sampling	10-01-2020	
			Date of Testing	10-01-2020	
IS Sieve Size	Weight Retained	Cum. Weight Retained	Cum. % Retained	Cum. % Passing	Spec. Limit (%) Passing (Zone-II)
10.00 mm	0	0	0	100.00	100
4.75 mm	236	236	7.87	92.13	90 - 100
2.36 mm	272	508	16.93	83.07	75 - 100
1.18 mm	516	1024	34.13	65.87	55 - 90
0.600 mm	546	1570	52.33	47.67	35 - 59
0.300 mm	672	2242	74.73	25.27	8-30
0.150 mm	530	2772	92.40	7.60	0 - 10
Pan	228	3000			-


Remarks :

Satisfactory / Not Satisfactory

Note:


1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

Consultant's Representative

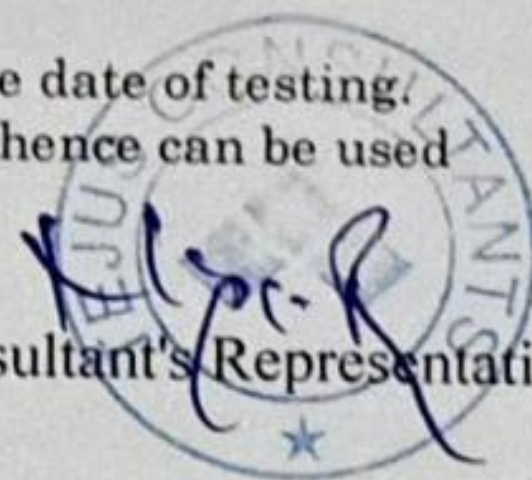

TEJUS CONSULTANTS

No. 5B, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, O : +91 80 23287532, tejusconsultants@gmail.com

TEST REPORT						
Clients	BRUHAT BENGALORE MAHANAGARA PALIKE					
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11					
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore					
Contractor	M/s Sri. E Ramesh Anand					
SPECIFIC GRAVITY AND WATER ABSORPTION FINE AGGREGATE (IS-2386-PART-3)						
Type of Material	M sand	Proposed Use			Concrete	
Location/Source	At Plant	Date of Sampling			10-01-2020	
Period of Soaking	24 hours	Date of Testing			11-01-2020	
Sl. No.	Test Property	TRIAL - 1	TRIAL - 2	TRIAL - 3	Average	
A	Weight of sturated surface dry sample gm.	664	668	662		
B	Weight of oven - dry sample gm.	656	660	654		
C	Weight of Pycnometer Filled with water gm	1275	1275	1275		
D	Weight of Pycnometer + sample + water gm	1693	1694	1692		
E	Bulk specific gravity B	2.667	2.651	2.669	2.662	
	(C + A - D)					
G	Absorption (%)	1.220	1.212	1.223	1.218	
	(A - B) *100 B					
Remarks : Satisfactory / Not Satisfactory						
Note: 1. The report shall not be reproduced, except in full, without the written approval of the laboratory. 2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site. 3. Any Query regarding the report must be reported reported within 15days from the date of testing. 4.The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.						
						Consultant's Representative






TEJUS
CONSULTANTS

Test Report on Compressive Strength of Concrete Cubes

Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11							
Client	Bruhat Bangalore Mahanagar Palike							
Consultant	TEJUS CONSULTANTS							
Contractor	M/s Sri.E Ramesh Anand							
Location:	Cement							
Grade of concrete:	M30							
Size of cube:	150x150x150 mm							
Reference IS code:	IS:516-1959							
Sl.No.	Date of Casting	Date of testing	Age of Test	Weight of Cube	Area of Cube	Failure load	Compressive strength	Avg. Compressive strength
				Kg	mm ²	KN	N/mm ²	N/mm ²
1	10-01-2020	07-02-2020	28 days	8.586	22500	678	30.13	30.49
2	10-01-2020	07-02-2020	28 days	8.742	22500	684	30.40	
3	10-01-2020	07-02-2020	28 days	8.566	22500	696	30.93	
Remarks : ☒ Satisfactory / Not Satisfactory								

Consultant's Representative

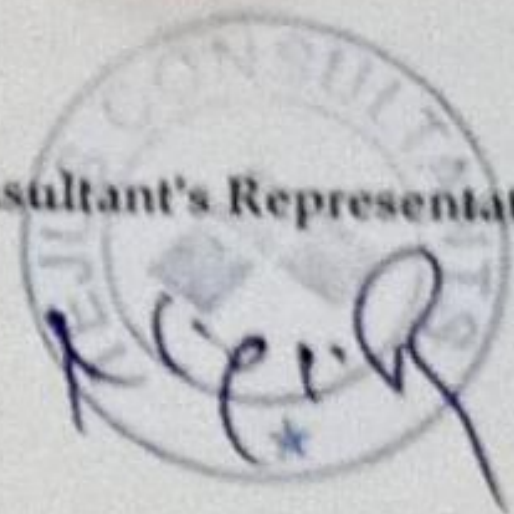

TEJUS CONSULTANTS

No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, D : +91 80 23287532, tejusconsultants@gmail.com



Test Report on Compressive Strength of Concrete Cubes

TEJUS

Project: Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11

Client: Bruhat Bangalore Mahanagar Palike

Consultant: TEJUS CONSULTANTS

Contractor: M/s Sri.E Ramesh Anand

Location: Cement

Grade of concrete: M30

Size of cube: 150x150x150 mm


Reference IS code: IS:516-1959

Sl.No.	Date of Casting	Date of testing	Age of Test	Weight of Cube	Area of Cube	Failure load	Compressive strength	Avg. Compressive strength
				Kg	mm ²	KN	N/mm ²	N/mm ²
1	10-01-2020	17-01-2020	7 days	8.742	22500	438	19.47	19.64
2	10-01-2020	17-01-2020	7 days	8.652	22500	442	19.64	
3	10-01-2020	17-01-2020	7 days	8.548	22500	446	19.82	

Remarks : Satisfactory / Not Satisfactory

[Signature]

Consultant's Representative

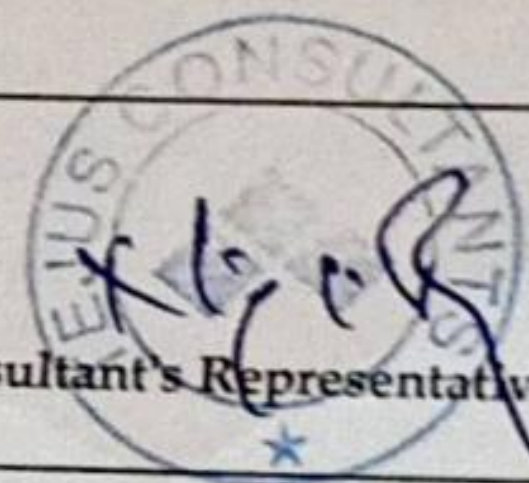


TEJUS CONSULTANTS

No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, O : +91 80 23287532, tejusconsultants@gmail.com


TEST REPORT					
Clients	Bruhat Bangalore Mahanagara Palike				
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11				
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore				
Contractor	M/s Sri. E Ramesh Anand				
Total Weight:	10000	gms			
SIEVE ANALYSIS					
Type of Material	20 mm down size		Proposed Use	Concrete	
Sample Location	At Plant		Date of Sampling	10-01-2020	
			Date of Testing	10-01-2020	
IS Sieve Size	Weight Retained	Cum. Weight Retained	Cum. % Retained	Cum. % Passing	Spec. Limit (%) Passing
40.00 mm	0	0	0	100	100
20.00 mm	272	272	2.72	97.28	95 - 100
10.00 mm	4972	5244	52.44	47.56	25 - 55
4.75 mm	4320	9564	95.64	4.36	0 - 10
Pan	436	10000			
Remarks : ☒ Satisfactory / Not Satisfactory					
Note:					

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

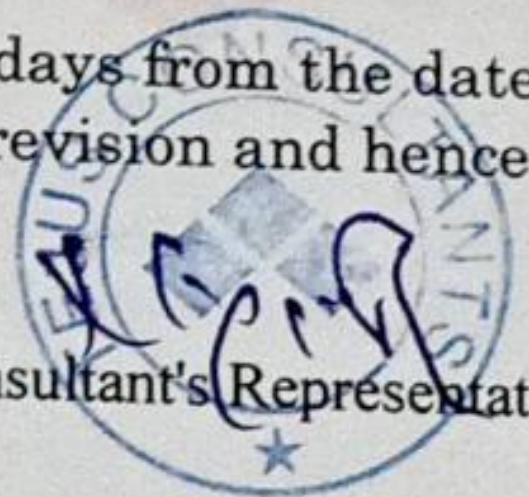Consultant's Representative

TEST REPORT

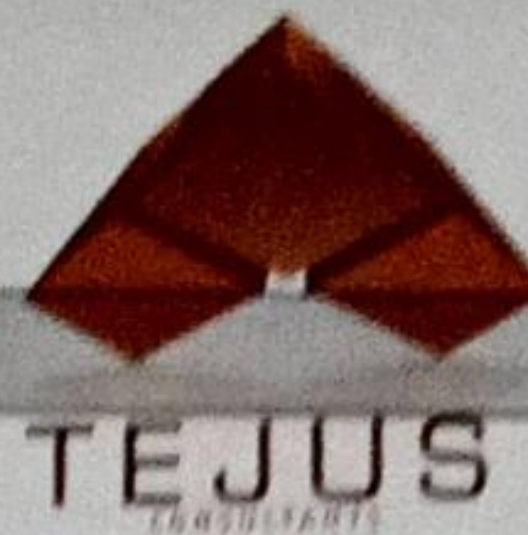

Clients	Bruhat Bangalore Mahanagara Palike	
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11	
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore	
Contractor	M/s Sri. E Ramesh Anand	
Total Weight:	10000	gms

SIEVE ANALYSIS

Type of Material	12.5 mm down size		Proposed Use	Concrete	
Sample Location	Plant		Date of Sampling	10-01-2020	
			Date of Testing	10-01-2020	
IS Sieve Size (in mm)	Weight Retained	Cum. Weight Retained	Cum. % Retained	Cum. % Passing	Spec. Limit (%) Passing
20.0	0	0	0	100	100
12.5	594	594	5.94	94.06	90-100
10.0	3344	3938	39.38	60.62	40-85
4.75	5426	9364	93.64	6.36	0-10
Pan	636	10000			


Remarks :

✓ Satisfactory / Not Satisfactory

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

Consultant's Representative

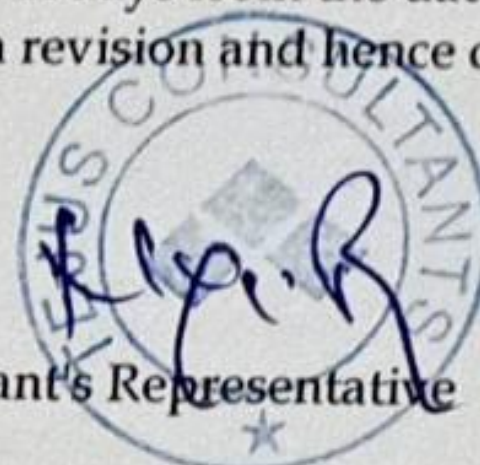

TEJUS CONSULTANTS

No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, Q : +91 80 23287532, tejusconsultants@gmail.com

Test Report on Cement

Project	Improvements to Roads and Drains at Lakkappa Layout, Singapuram Panchayat, Hosahalli Nagar, MS Panchayat, Vinayaka Nagar and Raghuram Layout in Ward No. 11			
Client	Bruhat Bangalore Mahanagar Palike			
Consultant	TEJUS CONSULTANTS			
Contractor	M/s Sri. E. Ramesh Anand			
Sample ID	Cement (ACC Cement) OPC 43 Grade			
Date of Sample Tested	10-01-2020			
Sample Supplied By	Agency			
Sl.No.	Descriptions	Test Method as per IS	Test Result	Requirements as per IS: 12269-1987
1	a) Initial Setting Time	IS-4031 (Part-5)	125 Minutes	Not Less than 30 Minutes
	b) Final Setting Time	IS-4031 (Part-5)	428 Minutes	Not More than 600 Minutes
2	Soundness	IS-4031 (Part-3) By the Le-Chatelier method	3mm	Not More than 10 mm
3	Standard Consistency	IS-4031 (Part-4)	26.00%	

Remarks :


Satisfactory / Not Satisfactory

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

[Signature]


Consultant's Representative

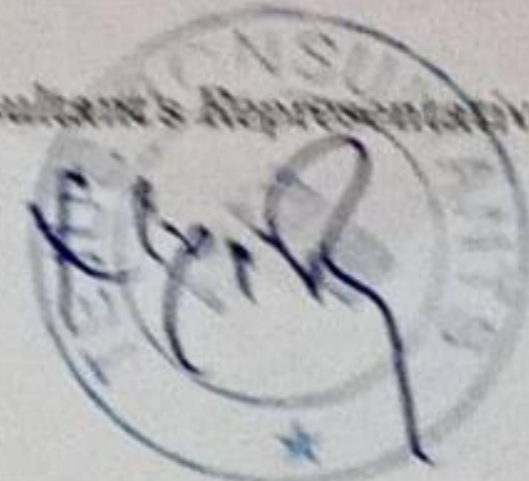

TEJUS CONSULTANTS


No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, O : +91 90 83287532, tejusconsultants@gmail.com

TEST REPORT	
Clients	Bruhat Bangalore Mahanagara Palike
Project	Improvements to Roads and Drains at Lakkappa Layout, Singasara Park, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No. 11
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore
Contractor	M/s Sri.E Ramesh Anand

SIEVE ANALYSIS					
Total Weight:	3000	gms			
Type of Material	Fine aggregate (River Sand/M sand)		Proposed Use	P.C.C	
Sample Location	At Plant/site		Date of Sampling	17-01-2020	
			Date of Testing	17-01-2020	
IS Sieve Size	Weight Retained	Cum. Weight Retained	Cum. % Retained	Cum. % Passing	Spec. Limit (%) Passing (Zone-II)
10.00 mm	0	0	0	100.00	100
4.75 mm	226	226	7.53	92.47	90 - 100
2.36 mm	288	514	17.13	82.87	75 - 100
1.18 mm	530	1044	34.80	65.20	55 - 90
0.600 mm	474	1518	50.60	49.40	35 - 59
0.300 mm	652	2170	72.33	27.67	8-30
0.150 mm	612	2782	92.73	7.27	0 - 10
Pan	218	3000			-
Remarks :  Satisfactory / Not Satisfactory					

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.




Consultant's Representative

TEJUS CONSULTANTS

No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwar Nagar, Bangalore - 560079, D: +91 80 23287532, tejusconsultants@gmail.com

Test Report on Cement



Project	Improvements to Roads and Drains at Lakkappa Layout, Singapore Paradise, Honabalu Nagara, MS Palya Vingayka Nagara and Raghuram Layout in Ward No.11			
Client	Bruhat Bangalore Mahanagar Palike			
Consultant	TEJUS CONSULTANTS			
Contractor	M/s Sri E Ramesh Anand			
Sample ID	Cement			
Date of Sample Tested	17-01-2020			
Sample Supplied By	Agency			
SLNo.	Descriptions	Test Method as per IS	Test Result	Requirements as per IS: 12269 1987
1	a) Initial Setting Time	IS-4031 (Part-5)	105 Minutes	Not Less than 30 Minutes
	b) Final Setting Time	IS-4031 (Part-5)	486	Not More than 600 Minutes
2	Soundness	IS-4031 (Part-3) By the Le-Chatelier method	6mm	Not More than 10 mm
3	Standard Consistency	IS-4031 (Part-4)	29.00%	
Remarks :		Satisfactory / Not Satisfactory		
Consultant's Representative				



TEJUS CONSULTANTS

No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, O : +91 80 23287532, tejusconsultants@ig

TEST REPORT						
Client's	Bruhat Bangalore Mahanagara Palike					
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11					
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore					
Contractor	M/s Sri.E Ramesh Anand					
SPECIFIC GRAVITY AND WATER ABSORPTION FINE AGGREGATE (IS-2386-PART-3)						
Type of Material	M sand			Proposed Use	P.C.C	
Location/Source	At Laboratory			Date of Sampling	17-01-2020	
Period of Soaking	24 hours			Date of Testing	18-01-2020	
Sl. No.	Test Property	TRIAL - 1	TRIAL - 2	TRIAL - 3	Average	
A	Weight of saturated surface dry sample gm.	675	668	650		
B	Weight of oven - dry sample gm.	668	659	640		
C	Weight of Pycnometer Filled with water gm	1275	1275	1275		
D	Weight of Pycnometer + sample + water gm	1698	1696	1684		
E	Bulk specific gravity B					
	(C + A - D)	2.651	2.668	2.656	2.658	
G	Absorption (%)					
	(A - B) *100	1.048	1.366	1.563	1.325	
	B					

Remarks :

✓ Satisfactory / Not Satisfactory

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

[Signature]

[Signature]
Consultant's Representative

TEST REPORT

Clients	Bruhat Bangalore Mahanagara Palike
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore
Contractor	M/s Sri. E Ramesh Anand
Total Weight:	10000 gms

SIEVE ANALYSIS


Type of Material	20 mm down size		Proposed Use	Concrete	
Sample Location	At Plant		Date of Sampling	23-01-2020	
			Date of Testing	23-01-2020	
IS Sieve Size	Weight Retained	Cum. Weight Retained	Cum. % Retained	Cum. % Passing	Spec. Limit (%) Passing
40.00 mm	0	0	0	100	100
20.00 mm	292	292	2.92	97.08	95 - 100
10.00 mm	4652	4944	49.44	50.56	25 - 55
4.75 mm	4574	9518	95.18	4.82	0 - 10
Pan	482	10000			

Remarks :

✓ Satisfactory / Not Satisfactory

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

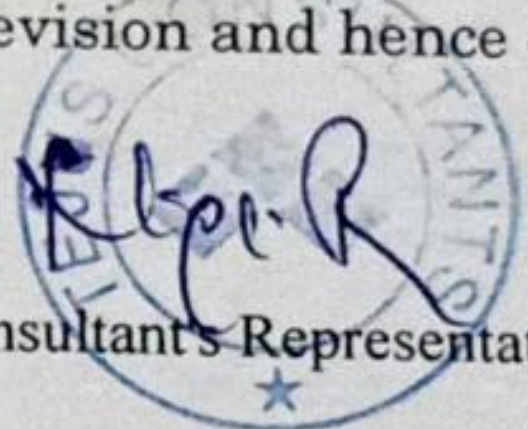Consultant's Representative



TEJUS

Test Report on Compressive Strength of Concrete Cube								
Project	Improvement in Road and Drains at Lakshmi Nagar, Singapore Roadside, Roadside Nagar, 100 Feet							
Client	M/s. Raghavendra Engineering Works							
Consultant	TEJUS CONSULTANTS							
Contractor	M/s. S. S. Ramani & Sons							
Location	Cement							
Grade of concrete	M30							
Size of cube	150x150x150 mm							
Reference to code	IS-516-1959							
Sl. No.	Date of Casting	Date of testing	Age of Test	Weight of Cube	Area of Cube	Failure load	Compressive strength	Avg. Compressive strength
				Kg	mm ²	KN	N/mm ²	N/mm ²
1	22-1-2020	20-12-2020	28 days	8.586	22500	681	30.27	30.58
2	22-1-2020	20-12-2020	28 days	8.766	22500	694	30.84	
3	22-1-2020	20-12-2020	28 days	8.562	22500	689	30.62	
Remarks : ☒ Satisfactory / ☐ Not Satisfactory								

46

Consultant's Representative




TEJUS CONSULTANTS

No. 68, 2nd floor, 2nd Cross, 2nd Stage, 4th Cross, Rajawade Nagar, Bangalore - 560079, India. Tel: 98 20 20 70 70, Fax: 98 20 20 70 70, www.tejusconsultants.com



Test Report on Cement

TEJUS

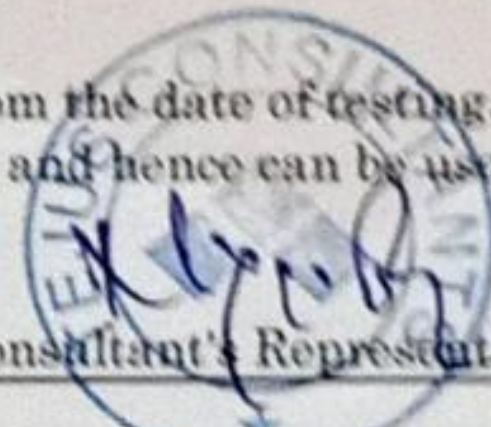Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11			
Client	Bruhat Bangalore Mahanagar Palike			
Consultant	TEJUS CONSULTANTS			
Contractor	M/s Sri. E Ramesh Anand			
Sample ID	Cement (ACC Cement) OPC 43 Grade			
Date of Sample Tested	23-01-2020			
Sample Supplied By	Agency			
SL.No.	Descriptions	Test Method as per IS	Test Result	Requirements as per IS: 12269-1987
1	a) Initial Setting Time	IS-4031 (Part-5)	104 Minutes	Not Less than 30 Minutes
	b) Final Setting Time	IS-4031 (Part-5)	386	Not More than 600 Minutes
2	Soundness	IS-4031 (Part-3) By the Le-Chatelier method	4mm	Not More than 10 mm
3	Standard Consistency	IS-4031 (Part-4)	30.00%	
Remarks :		✓ Satisfactory / Not Satisfactory		
Note: 1. The report shall not be reproduced, except in full, without the written approval of the laboratory. 2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site. 3. Any Query regarding the report must be reported reported within 15days from the date of testing. 4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.  Consultant's Representative				

Test Report on Cement



Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11
Client	Bruhat Bangalore Mahanagar Palike
Consultant	TEJUS CONSULTANTS
Contractor	M/s Sri E Ramesh Anand
Sample ID	Cement
Date of Sample Tested	17-01-2020
Sample Supplied By	Agency

Sl.No.	Descriptions	Test Method as per IS	Test Result	Requirements as per IS: 12269-1987
1	a) Initial Setting Time	IS-4031 (Part-5)	105 Minutes	Not Less than 30 Minutes
	b) Final Setting Time	IS-4031 (Part-5)	486	Not More than 600 Minutes
2	Soundness	IS-4031 (Part-3) By the Le-Chatelier method	6mm	Not More than 10 mm
3	Standard Consistency	IS-4031 (Part-4)	29.00%	

Remarks :

✓ Satisfactory / Not Satisfactory

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.



TEST REPORT		
Clients	Bruhat Bangalore Mahanagara Palike	
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11	
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore	
Contractor	M/s Sri. E Ramesh Anand	
Total Weight:	10000	gms

TEJUS
CONSULTANTS

SIEVE ANALYSIS

Type of Material	12.5 mm down size		Proposed Use	Concrete	
Sample Location	Plant		Date of Sampling	23-01-2020	
			Date of Testing	23-01-2020	
IS Sieve Size (in mm)	Weight Retained	Cum. Weight Retained	Cum. % Retained	Cum. % Passing	Spec. Limit (%) Passing
20.0	0	0	0	100	100
12.5	574	574	5.74	94.26	90-100
10.0	3384	3958	39.58	60.42	40-85
4.75	5482	9440	94.40	5.60	0-10
Pan	560	10000			

Remarks :


Satisfactory / Not Satisfactory

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

[Signature]

Consultant's Representative

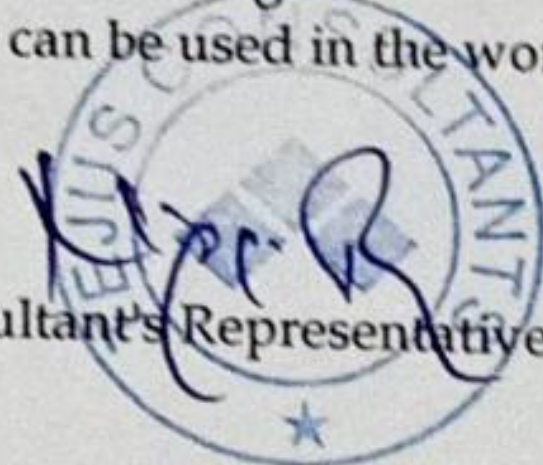

TEJUS CONSULTANTS

No. 5B, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, O : +91 80 23287532, tejusconsultants@gmail.c



Test Report on Cement

TEJUS


Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11			
Client	Bruhat Bangalore Mahanagar Palike			
Consultant	TEJUS CONSULTANTS			
Contractor	M/s Sri. E Ramesh Anand			
Sample ID	Cement (ACC Cement) OPC 43 Grade			
Date of Sample Tested	23-01-2020			
Sample Supplied By	Agency			
Sl.No.	Descriptions	Test Method as per IS	Test Result	Requirements as per IS: 12269-1987
1	a) Initial Setting Time	IS-4031 (Part-5)	104 Minutes	Not Less than 30 Minutes
	b) Final Setting Time	IS-4031 (Part-5)	386	Not More than 600 Minutes
2	Soundness	IS-4031 (Part-3) By the Le-Chatelier method	4mm	Not More than 10 mm
3	Standard Consistency	IS-4031 (Part-4)	30.00%	
Remarks :		✓ Satisfactory / Not Satisfactory		
Note: 1. The report shall not be reproduced, except in full, without the written approval of the laboratory. 2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site. 3. Any Query regarding the report must be reported reported within 15days from the date of testing. 4.The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.				

Consultant's Representative

TEJUS CONSULTANTS

No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, O : +91 80 23287532, tejusconsultants@gmail.com

TEST REPORT

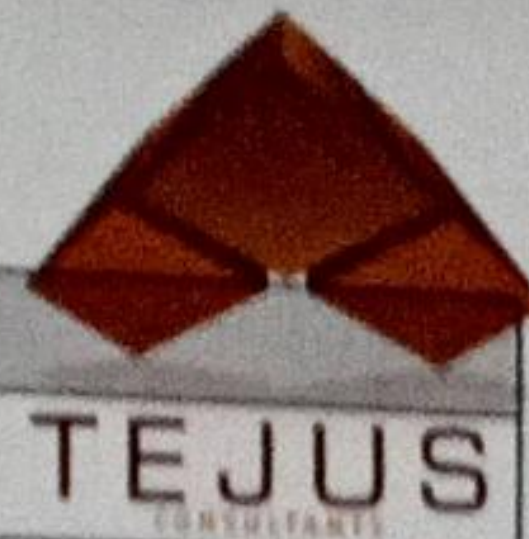

Clients	Bruhat Bangalore Mahanagara Palike
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore
Contractor	M/s Sri. E Ramesh Anand

SIEVE ANALYSIS

Total Weight:	3000	gms			
Type of Material	Fine aggregate (M sand)	Proposed Use	Concrete		
Sample Location	At Plant	Date of Sampling	23-01-2020		
		Date of Testing	23-01-2020		
IS Sieve Size	Weight Retained	Cum. Weight Retained	Cum. % Retained	Cum. % Passing	Spec. Limit (%) Passing (Zone-II)
10.00 mm	0	0	0	100.00	100
4.75 mm	218	218	7.27	92.73	90 - 100
2.36 mm	274	492	16.40	83.60	75 - 100
1.18 mm	424	916	30.53	69.47	55 - 90
0.600 mm	574	1490	49.67	50.33	35 - 59
0.300 mm	752	2242	74.73	25.27	8-30
0.150 mm	536	2778	92.60	7.40	0 - 10
Pan	222	3000			-


Remarks :

Satisfactory / Not Satisfactory

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

Consultant's Representative

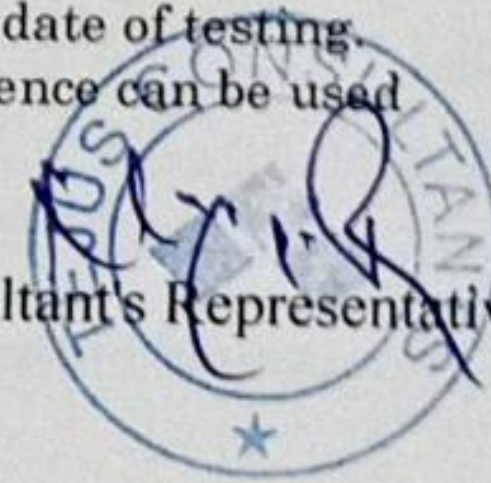

TEJUS CONSULTANTS

No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, O : +91 80 23287532, tejusconsultants@gmail.com

TEST REPORT

Clients	BRUHAT BENGALORE MAHANAGARA PALIKE
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore
Contractor	M/s Sri. E Ramesh Anand

SPECIFIC GRAVITY AND WATER ABSORPTION FINE AGGREGATE (IS-2386-PART-3)

Type of Material	M sand	Proposed Use	Concrete
Location/Source	At Plant	Date of Sampling	23-01-2020
Period of Soaking	24 hours	Date of Testing	24-01-2020

Sl. No.	Test Property	TRIAL - 1	TRIAL - 2	TRIAL - 3	Average
A	Weight of saturated surface dry sample gm.	646	653	664	
B	Weight of oven - dry sample gm.	638	645	655	
C	Weight of Pycnometer Filled with water gm	1275	1275	1275	
D	Weight of Pycnometer + sample + water gm	1682	1685	1692	
E	Bulk specific gravity $\frac{B}{(C + A - D)}$	2.669	2.654	2.652	2.659
G	Absorption (%) $\frac{(A - B) * 100}{B}$	1.254	1.240	1.374	1.289

Remarks :

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.

Satisfactory / Not Satisfactory

Consultant's Representative

TEST REPORT	
Clients	BRUHAT BENGALORE MAHANAGARA PALIKE
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11
Consultants	TEJUS CONSULTANTS Basaveshwar Nagar Bangalore
Contractor	M/s Sri. E Ramesh Anand

SPECIFIC GRAVITY AND WATER ABSORPTION
FINE AGGREGATE (IS-2386-PART-3)


Type of Material	M sand	Proposed Use			Concrete
Location/Source	At Plant	Date of Sampling			23-01-2020
Period of Soaking	24 hours	Date of Testing			24-01-2020
Sl. No.	Test Property	TRIAL - 1	TRIAL - 2	TRIAL - 3	Average
A	Weight of sturated surface dry sample gm.	646	653	664	
B	Weight of oven - dry sample gm.	638	645	655	
C	Weight of Pycnometer Filled with water gm	1275	1275	1275	
D	Weight of Pycnometer + sample + water gm	1682	1685	1692	
E	Bulk specific gravity $\frac{B}{(C + A - D)}$	2.669	2.654	2.652	2.659
G	Absorption (%) $\frac{(A - B) * 100}{B}$	1.254	1.240	1.374	1.289

Remarks :


Satisfactory / Not Satisfactory

Note:

1. The report shall not be reproduced, except in full, without the written approval of the laboratory.
2. The results indicated above are based on the tests carried out on the samples received in the laboratory /Site.
3. Any Query regarding the report must be reported reported within 15days from the date of testing.
4. The material used in the site satisfied the standard of MORTH's 5th revision and hence can be used in the work.



Consultant's Representative

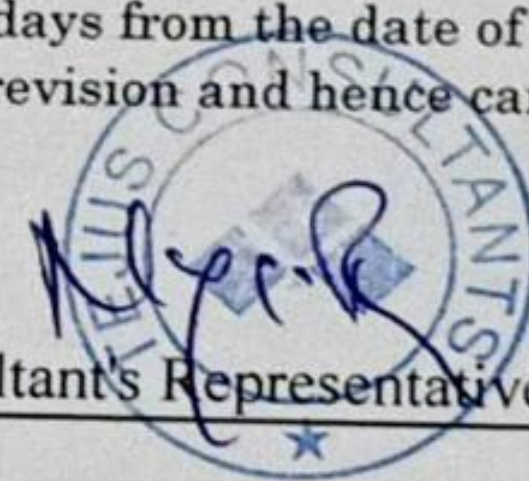



TEJUS

Test Report on Compressive Strength of Concrete Cubes								
Project	Improvements to Roads and Drains at Lakkappa Layout, Singapura Paradise, Hosabalu Nagara, MS Palya Vinayaka Nagara and Raghuram Layout in Ward No.11							
Client	Bruhat Bangalore Mahanagar Palike							
Consultant	TEJUS CONSULTANTS							
Contractor	M/s Sri.E Ramesh Anand							
Location:	Cement							
Grade of concrete:	M30							
Size of cube:	150x150x150 mm							
Reference IS code:	IS:516-1959							
Sl.No.	Date of Casting	Date of testing	Age of Test	Weight of Cube	Area of Cube	Failure load	Compressive strength	Avg. Compressive strength
				Kg	mm ²	KN	N/mm ²	N/mm ²
1	23-01-2020	30-01-2020	7 days	8.824	22500	446	19.82	19.59
2	23-01-2020	30-01-2020	7 days	8.794	22500	436	19.38	
3	23-01-2020	30-01-2020	7 days	8.658	22500	440	19.56	
Remarks : ☒ Satisfactory / ☐ Not Satisfactory								
 Consultant's Representative								

TEJUS CONSULTANTS

No. 58, 3rd main, 6th Cross, 1st Stage KHB Colony, Basaveshwaranagar, Bangalore - 560079, O : +91 80 23287532, tejusconsultants@gmail.com
